ID	Task Mode	Task Name	Duration	Start	Finish	% Complete	Actual Start	Actual Finish	Predecessors
1		**Customer A Build - xxx**	**89 days**	**Fri 3/3/17**	**Wed 7/5/17**	**0%**	**NA**	**NA**	
2		**Package A - Structural and Pathways**	**40 days**	**Fri 3/3/17**	**Thu 4/27/17**	**0%**	**NA**	**NA**	
3		Design	10 days	Fri 3/3/17	Thu 3/16/17	0%	NA	NA	
4		Materials Procurement	10 days	Fri 3/17/17	Thu 3/30/17	0%	NA	NA	3FF+10 days
5		Materials PO	0 days	Thu 3/30/17	Thu 3/30/17	0%	NA	NA	4
6		Materials Delivery	1 day	Thu 4/6/17	Thu 4/6/17	0%	NA	NA	4FF+5 days
7		Package A Build	15 days	Fri 4/7/17	Thu 4/27/17	0%	NA	NA	6
8		**Package B - Electrical**	**71 days**	**Fri 3/3/17**	**Fri 6/9/17**	**0%**	**NA**	**NA**	
9		Design	15 days	Fri 3/3/17	Thu 3/23/17	0%	NA	NA	
10		Stamped Electrical Permit Design	8 days	Fri 3/24/17	Tue 4/4/17	0%	NA	NA	9
11		Materials Ordered	0 days	Thu 4/6/17	Thu 4/6/17	0%	NA	NA	9FF+10 days
12		Materials Delivery	1 day	Fri 5/5/17	Fri 5/5/17	0%	NA	NA	11FS+20 days
13		Permits	8 days	Wed 4/5/17	Fri 4/14/17	0%	NA	NA	10
14		Package B Build - Busway Install/Commission, Grounding Grid	20 days	Mon 5/8/17	Fri 6/2/17	0%	NA	NA	12,13
15		Electrical Commissioning	5 days	Mon 6/5/17	Fri 6/9/17	0%	NA	NA	14
16		**Containmet**	**43 days**	**Fri 3/24/17**	**Tue 5/23/17**	**0%**	**NA**	**NA**	
17		Containment Design	5 days	Fri 3/24/17	Thu 3/30/17	0%	NA	NA	3,9
18		Containment Materials Ordered	8 days	Fri 3/31/17	Tue 4/11/17	0%	NA	NA	17
19		Containment Materials Delivered	15 days	Wed 4/12/17	Tue 5/2/17	0%	NA	NA	18
20		Containment Build	15 days	Wed 5/3/17	Tue 5/23/17	0%	NA	NA	19
21		**Package C - Cabinets/LVC**	**81 days**	**Fri 3/3/17**	**Fri 6/23/17**	**0%**	**NA**	**NA**	
22		Cabinet Layout Design	5 days	Fri 3/3/17	Thu 3/9/17	0%	NA	NA	
23		Inter-Room Connectivity Design	5 days	Fri 3/10/17	Thu 3/16/17	0%	NA	NA	22
24		LVC Design	10 days	Fri 3/10/17	Thu 3/23/17	0%	NA	NA	22
25		Cabinet/Patch Rack Materials Ordered	8 days	Fri 3/24/17	Tue 4/4/17	0%	NA	NA	22FS+10 days
26		Inter-Room Materials Ordered	8 days	Tue 3/21/17	Thu 3/30/17	0%	NA	NA	23FF+10 days
27		LVC Materials ordered	8 days	Tue 3/28/17	Thu 4/6/17	0%	NA	NA	24FF+10 days
28		Cabinet Materials Delivered	1 day	Tue 5/2/17	Tue 5/2/17	0%	NA	NA	25FF+20 days
29		Inter-Room Materials Delivered	1 day	Thu 4/27/17	Thu 4/27/17	0%	NA	NA	26FF+20 days
30		LVC Materials Delivered	1 day	Thu 5/4/17	Thu 5/4/17	0%	NA	NA	27FF+20 days
31		Inter-Room Connectivity Labor - Installation/Testing	10 days	Fri 4/28/17	Thu 5/11/17	0%	NA	NA	29
32		LVC Labor - Installation/Testing	15 days	Mon 6/5/17	Fri 6/23/17	0%	NA	NA	30,14,7SS+5 days
33		Room DC Eng Ready	0 days	Fri 6/23/17	Fri 6/23/17	0%	NA	NA	2,8,31,32
34		**DC Eng - Build out**	**8 days**	**Mon 6/26/17**	**Wed 7/5/17**	**0%**	**NA**	**NA**	
35		Cabinet Grounding	2 days	Mon 6/26/17	Tue 6/27/17	0%	NA	NA	33
36		Console Cables Run	2 days	Mon 6/26/17	Tue 6/27/17	0%	NA	NA	33
37		Management Cables Run	4 days	Wed 6/28/17	Mon 7/3/17	0%	NA	NA	36
38		Fabric Breakout patches	5 days	Mon 6/26/17	Fri 6/30/17	0%	NA	NA	33
39		Patch Cord Labeling	2 days	Tue 7/4/17	Wed 7/5/17	0%	NA	NA	36,37
40		Room IT Hardware Ready	0 days	Tue 7/4/17	Tue 7/4/17	0%	NA	NA	39FS-2 days

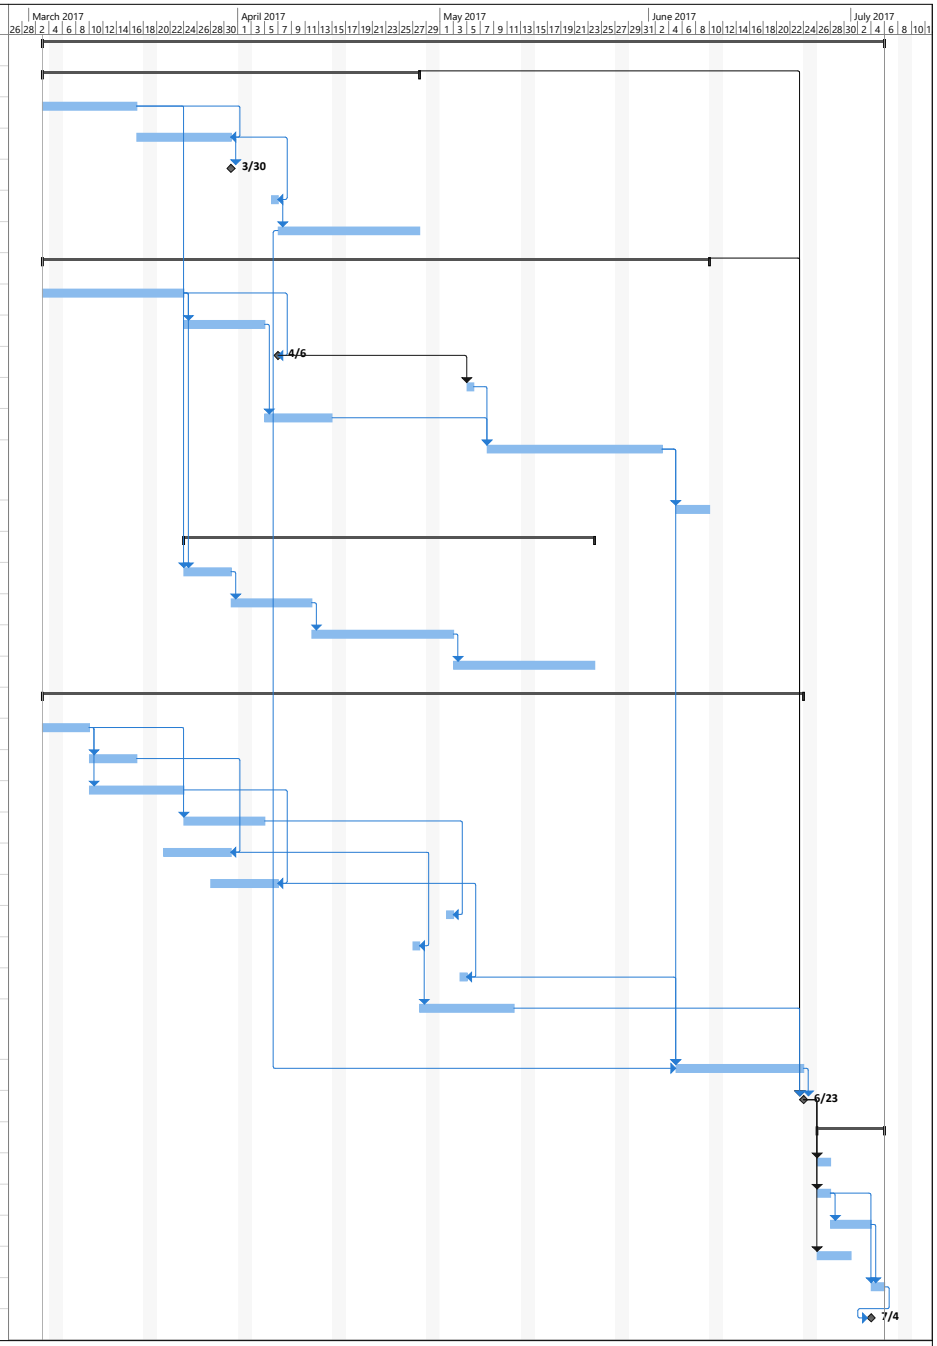

Project: SFDC Build Project Schedu
Date: Thu 11/16/17

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
