



Safety Moment

Schedule

The Pressure Cooker Concept


Pressure Cooker Concept

- Typically occurs when a project is 60% complete
- Recognition project end date is in jeopardy
- Project challenged to complete on time



Schedule Pressure

Run to the finish
Focus on individual targets
Decreased collaboration
Cutting Corners



Increased Resources

Safety Culture awareness
Congestion
Productivity Impacts



Stored Energy


Testing & Energization
Exclusion zone barriers



Increased Risk


Increased likelihood of serious
safety incidents

Pressure Cooker Concept

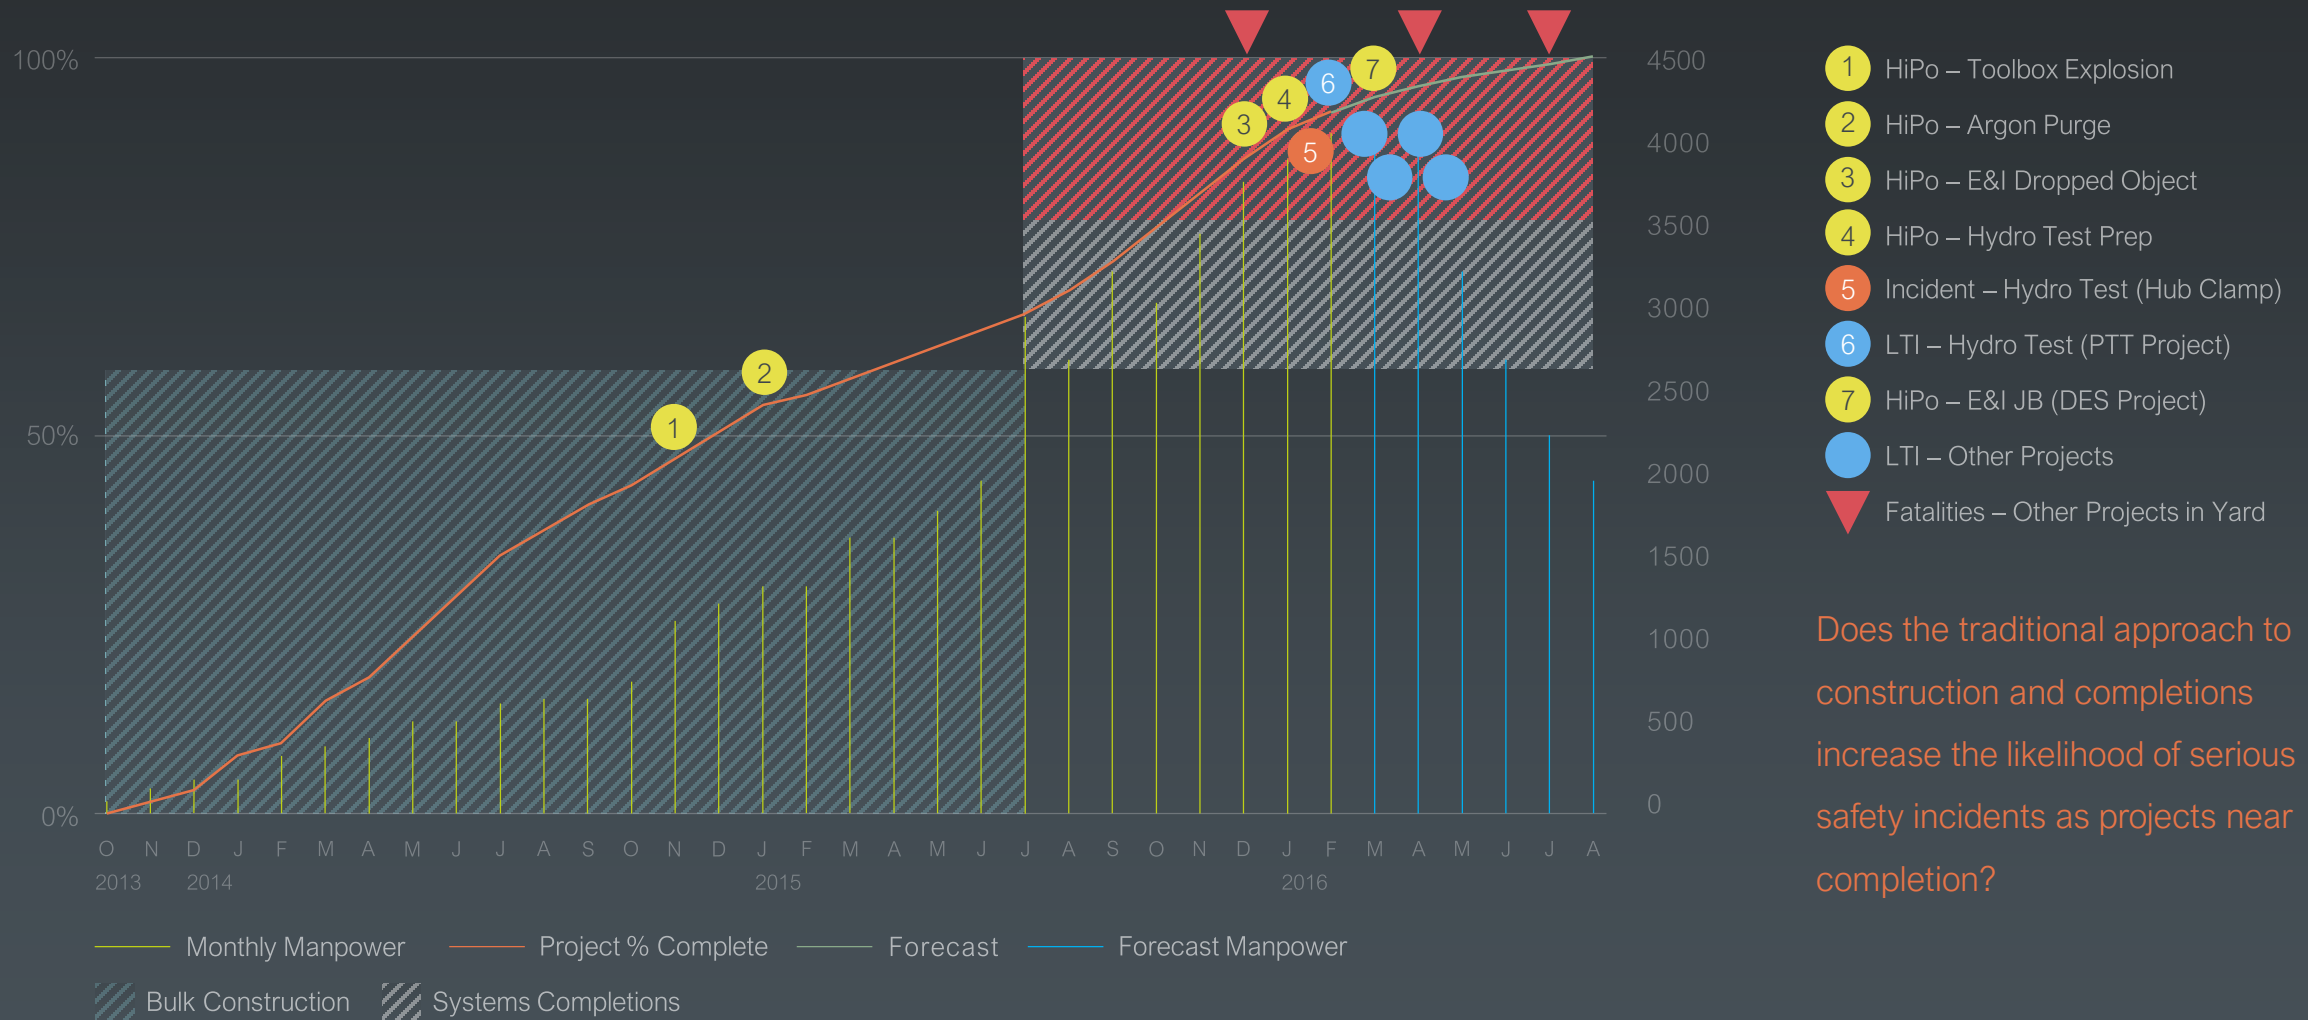

Does the traditional approach to construction and completions increase the likelihood of serious safety incidents as projects near completion?

Pressure Cooker Concept

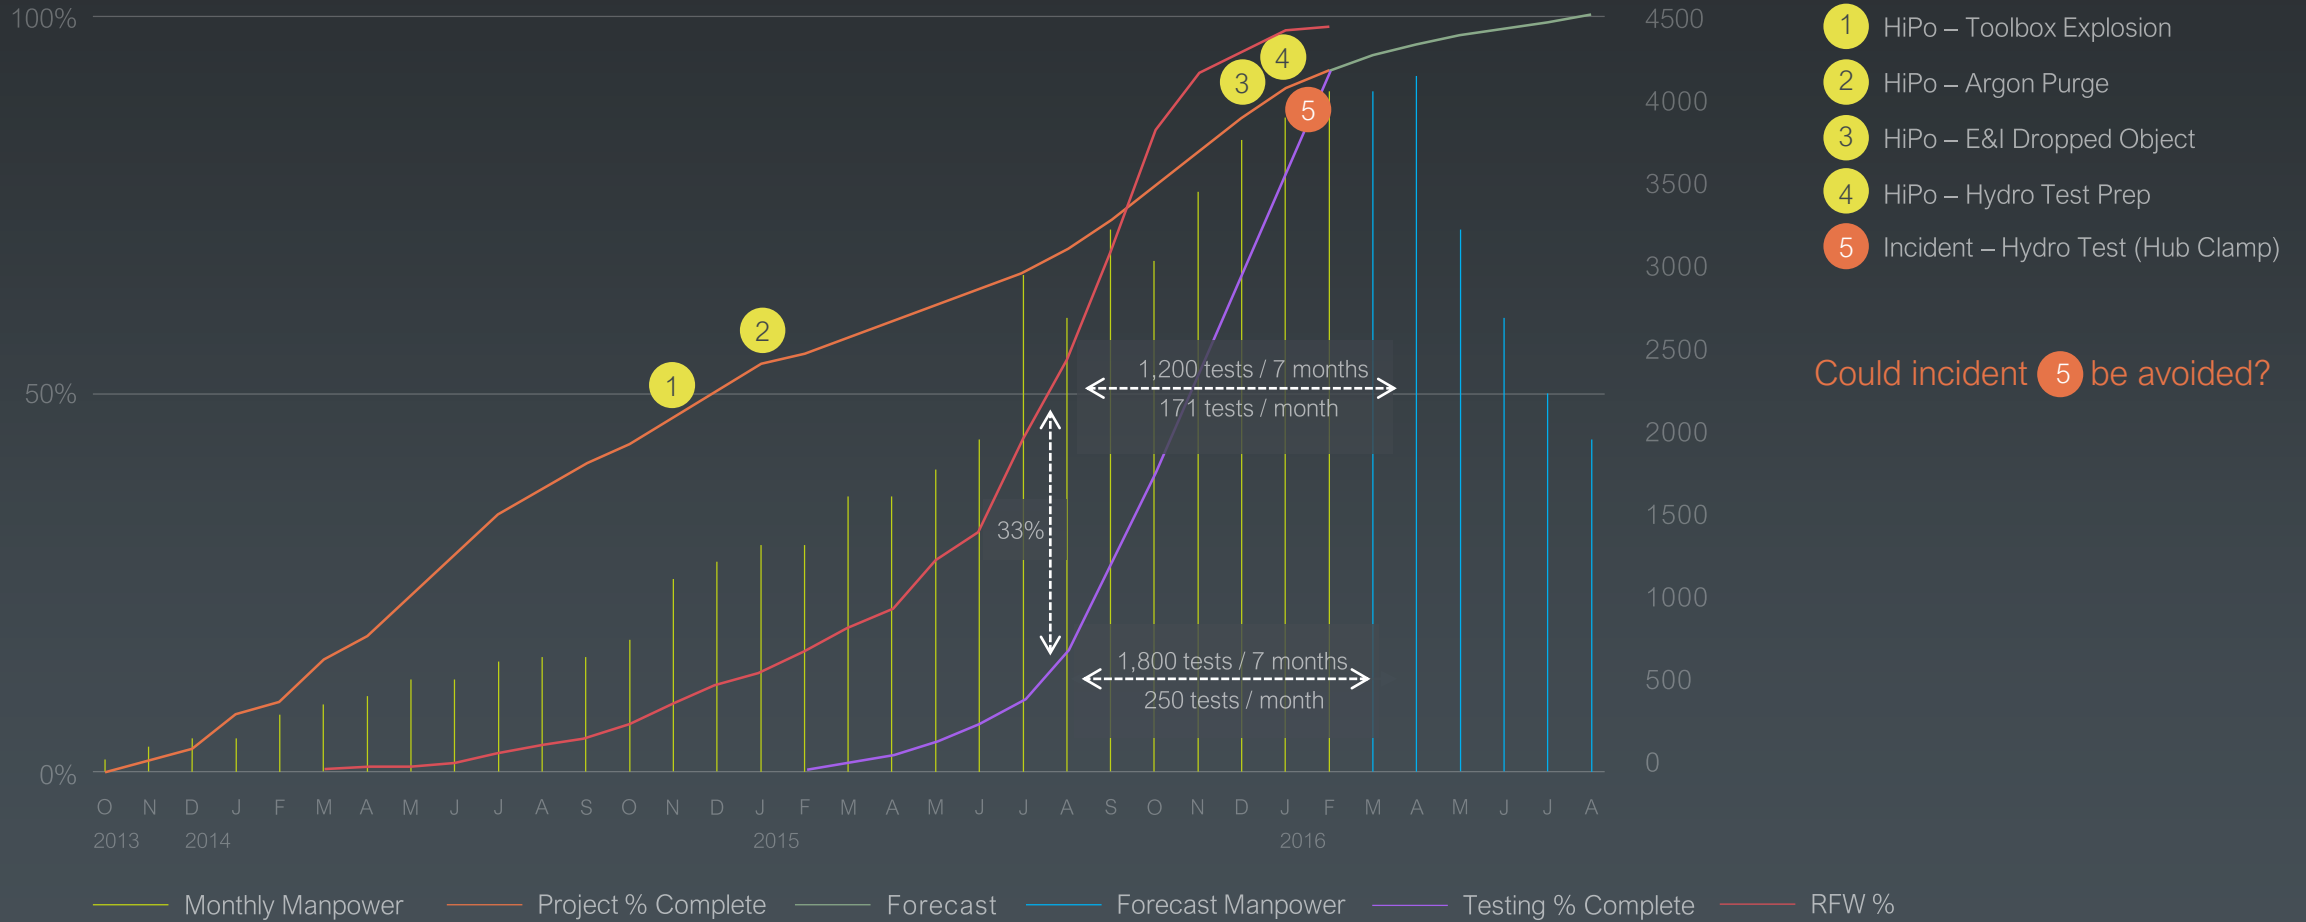

What to learn?

- Be aware of tight schedules
- Establish float in schedules (Safety valve)
- Allow Contractor to establish realistic plans
- Improve workfronts monitoring
- Improve multi discipline collaboration
- Extend schedule when necessary

